


- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone
- Summary

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish
Total		88.0	60.0	30/Mar/15 A	16/Jul/15
Construction		88.0	60.0	30/Mar/15 A	16/Jul/15
Addition		70.0	60.0	13/Apr/15 A	16/Jul/15
A2490	Columns & I Beams	2.0	0.0	13/Apr/15 A	14/Apr/15 A
A2520	Exterior Sheathing	5.0	0.0	13/Apr/15 A	22/Apr/15 A
A2500	Bar Joist & Misc. Steel	7.0	3.0	15/Apr/15 A	27/Apr/15
A2510	Metal Decking	3.0	0.0	21/Apr/15 A	22/Apr/15 A
A3290	Damproofing	4.0	4.0	21/Apr/15 A	28/Apr/15
A3010	Set RTU Curbs	2.0	2.0	23/Apr/15 A	24/Apr/15
A2640	Interior Stud Framing	5.0	5.0	23/Apr/15 A	29/Apr/15
A2910	Parapet Framing & Sheathing	5.0	5.0	23/Apr/15 A	29/Apr/15
A2920	TPO Roofing	4.0	4.0	28/Apr/15*	01/May/15
A2530	Brick Veneer & Rigid Insulation	15.0	15.0	29/Apr/15	19/May/15
A3020	Roof Blocking	2.0	2.0	30/Apr/15	01/May/15
A2690	Frame Bulkheads	5.0	5.0	30/Apr/15	06/May/15
A2700	PM&E In Wall Rough In	7.0	7.0	30/Apr/15	08/May/15
A3000	Set RTUs	2.0	2.0	04/May/15	05/May/15
A2650	Electrical Overhead Rough In	18.0	18.0	04/May/15	27/May/15
A2660	Plumbing Overhead Rough In	18.0	18.0	04/May/15	27/May/15
A2670	Mechanical Overhead Rough In	18.0	18.0	04/May/15	27/May/15
A3220	Fire Protection Overhead Rough In	18.0	18.0	04/May/15	27/May/15
A3030	Electrical to RTUs	5.0	5.0	06/May/15	12/May/15
A2710	Bulkhead Rough In	1.0	1.0	07/May/15	07/May/15
A3300	Fire Pump Room Construction	15.0	15.0	11/May/15*	29/May/15
A2720	In Wall Inspection	1.0	1.0	11/May/15	11/May/15
A3210	H&F Bulkheads	5.0	5.0	12/May/15	18/May/15
A2730	H&F Drywall Walls	15.0	15.0	12/May/15	01/Jun/15
A2610	Storefront / Folding Glass Wall	8.0	8.0	13/May/15	22/May/15
A3070	Set Panel Cans	1.0	1.0	14/May/15	14/May/15
A3080	Install New Electrical Panels	1.0	1.0	15/May/15	15/May/15
A3090	Pull Feeder Wire	2.0	2.0	18/May/15	19/May/15
A2630	Downspouts	2.0	2.0	20/May/15	21/May/15

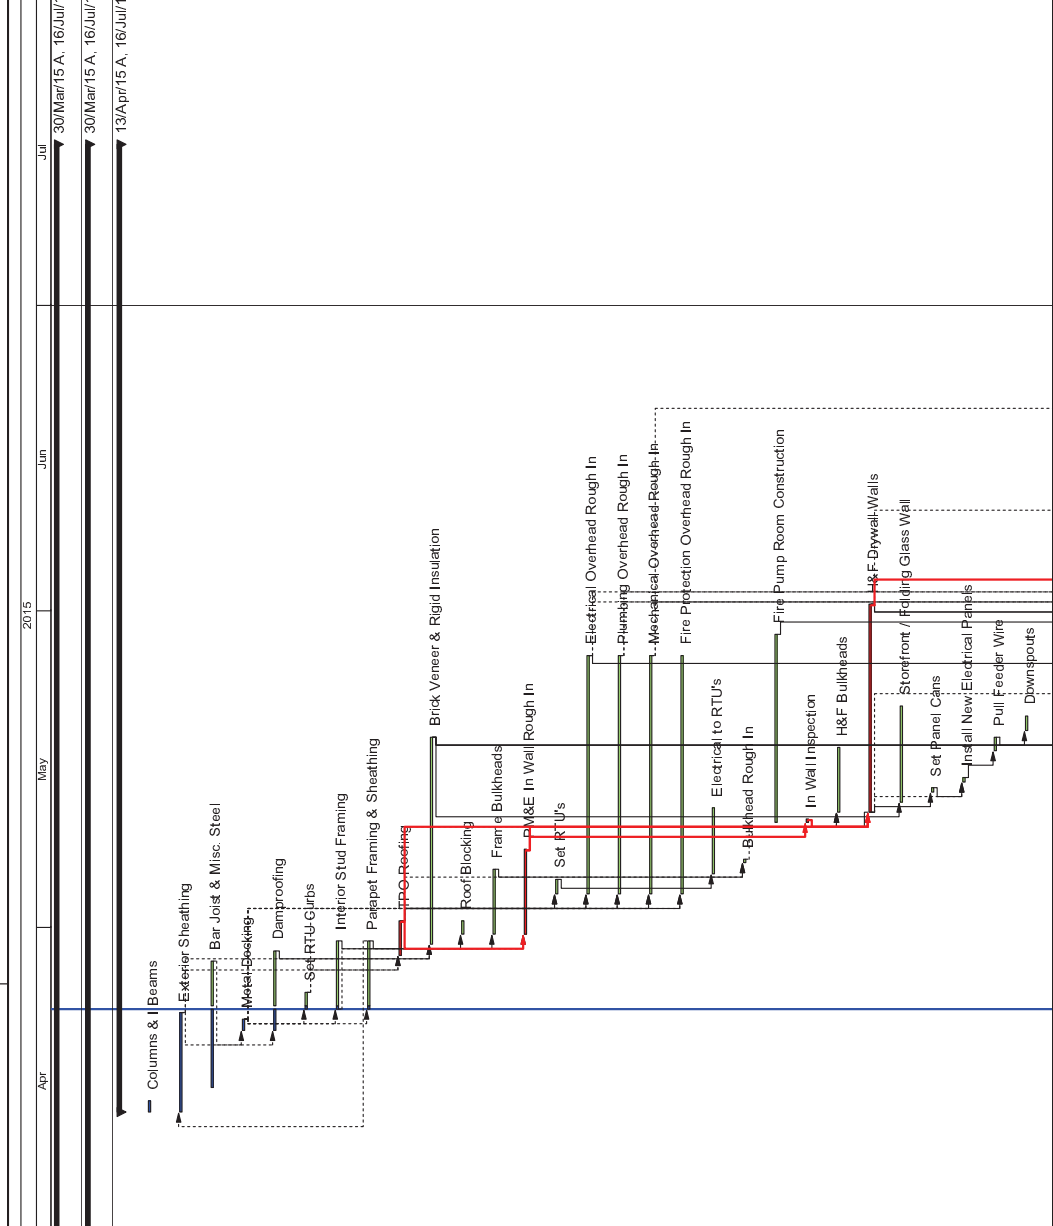


City of Greenville

Greenville Convention Center Expansion & Renovation

Greenville, North Carolina

- Date: 23/Apr/15
- Run Date: 23/Apr/15
- Finish Date: 16/Jul/15
- Page 1 of 6

- █ Actual Work
- █ Remaining Work
- █ Critical Remaining Work
- ◆ Milestone
- Summary

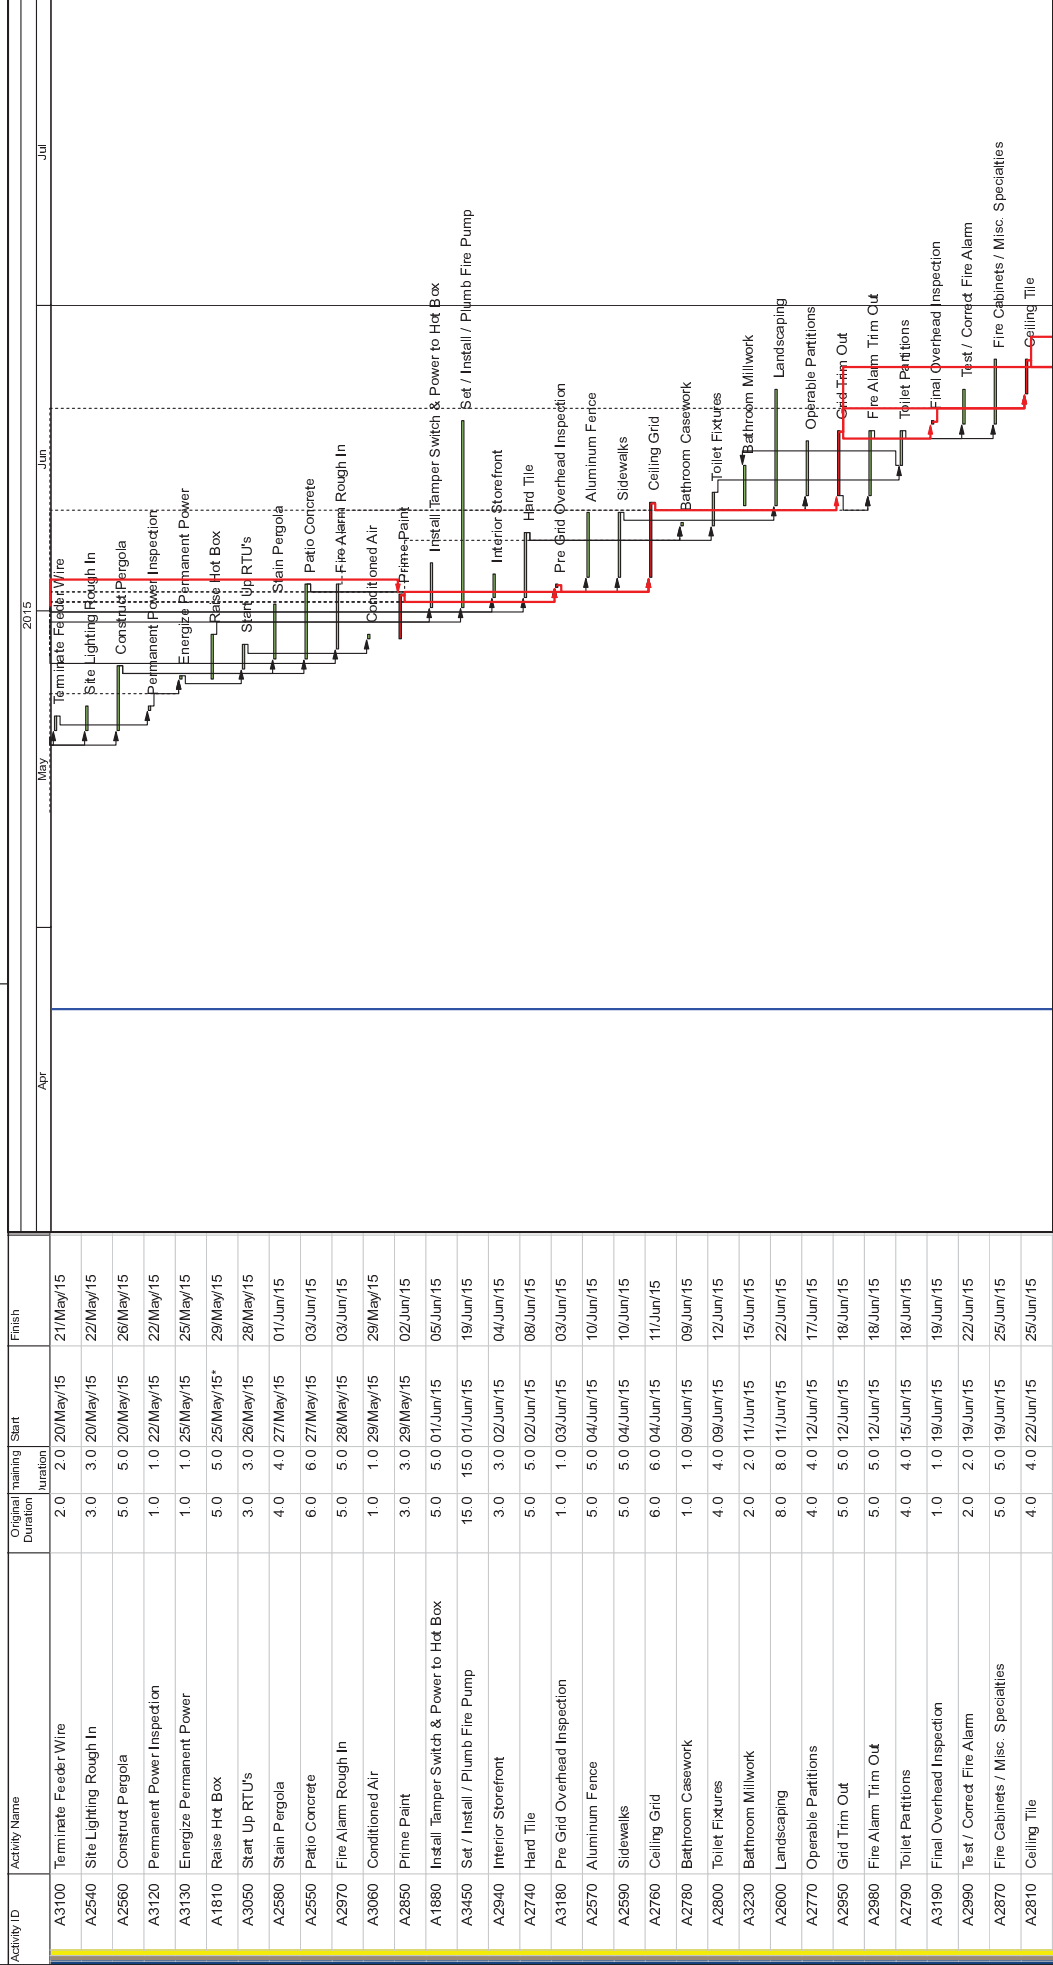

City of Greenville

Greenville Convention Center Expansion & Renovation

Greenville, North Carolina



- Date: 23/Apr/15
- Run Date: 23/Apr/15
- Finish Date: 16/Jul/15
- Page 2 of 6

- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone
- Summary

Activity ID	Activity Name	Original Duration	Training Duration	Start	Finish
A2750	VWC	7.0	7.0	22/June/15	30/June/15
A3150	Drywall Point Up	1.0	1.0	26/June/15	26/June/15
A2860	Final Paint	2.0	2.0	29/June/15	30/June/15
A2960	Wall Devices & Trim Out	2.0	2.0	29/June/15	30/June/15
A2880	Carpet	5.0	5.0	29/June/15	06/July/15
A2930	Rubber Base	3.0	3.0	02/July/15	07/July/15
A2820	Doors & Hardware	3.0	3.0	06/July/15	08/July/15
A2840	City of Greenville Inspections	3.0	3.0	09/July/15	13/July/15
A3160	Punch Out	5.0	5.0	09/July/15	15/July/15
A3200	Receive C. of O.	1.0	1.0	14/July/15	14/July/15
A2830	Furniture	2.0	2.0	15/July/15	16/July/15
Renovation					
		84.0	56.0	30/Mar/15 A	10/Jul/15
Gallery					
		63.0	35.0	30/Mar/15 A	10/June/15
A3380	F1 & F2 Lights Cable & Install	35.0	0.0	30/Mar/15 A	17/Apr/15 A
A3420	Fire Protection (Received Permit on 4/2)	38.0	25.0	09/Apr/15 A	27/May/15
A3350	Ceilings	27.0	27.0	28/Apr/15*	03/June/15
A3360	Diffusers	27.0	27.0	28/Apr/15	03/June/15
A3430	Metalic Paint @ MDF	3.0	3.0	04/May/15	06/May/15
A3340	Doors @ Entrances	5.0	5.0	04/May/15*	08/May/15
A3390	Ceiling Disk	15.0	15.0	21/May/15	10/June/15
A3410	Disk Lighting	15.0	15.0	21/May/15	10/June/15
A3440	Final Paint	5.0	5.0	04/June/15	10/June/15
Corridors					
		44.0	44.0	11/May/15	10/Jul/15
East Corridor					
		41.0	41.0	11/May/15	07/Jul/15
A4440	Lower Fire Protection	5.0	5.0	11/May/15*	15/May/15
A4550	Laminate Beams & Columns	5.0	5.0	11/May/15*	15/May/15
A3850	East Corridor Rough In Circle @ Concessions	2.0	2.0	18/May/15	19/May/15
A3870	East Corridor Demo Ceilings	2.0	2.0	18/May/15	19/May/15
A3860	East Corridor H&F Circle @ Concessions	2.0	2.0	20/May/15	21/May/15
A3880	East Corridor Extend Drywall to New Ceiling Height	4.0	4.0	20/May/15	25/May/15
A3890	East Corridor Demo VWC	5.0	5.0	20/May/15	26/May/15
A3900	East Corridor H&F Bulkheads Spanning Corridor	5.0	5.0	20/May/15	26/May/15



City of Greenville

Greenville Convention Center Expansion & Renovation

Greenville, North Carolina




- Date: 23/Apr/15
- Run Date: 23/Apr/15
- Finish Date: 16/Jul/15
- Page: 3 of 6

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- Summary

Activity ID	Activity Name	Original Duration	Training Duration	Start	Finish
A3920	East Corridor Paint Beneath Existing Storefront	2.0	2.0	27/May/15	28/May/15
A3910	East Corridor VWC	8.0	8.0	27/May/15	05/Jun/15
A3930	East Corridor Ceiling Grid	7.0	7.0	08/Jun/15	16/Jun/15
A3940	East Corridor Extend MEP to New Ceiling Height	7.0	7.0	11/Jun/15	19/Jun/15
A3950	East Corridor Ceiling Tile	4.0	4.0	22/Jun/15	25/Jun/15
A3960	East Corridor Demo Existing & Install New Flooring	7.0	7.0	26/Jun/15	07/Jul/15
	West Corridor	39.0	39.0	18/May/15	10/Jul/15
A4530	Lower Fire Protection	5.0	5.0	18/May/15	22/May/15
A4560	Laminate Beams & Columns	5.0	5.0	18/May/15	22/May/15
A4030	West Corridor Rough In Circle @ Concessions	2.0	2.0	25/May/15	26/May/15
A4050	West Corridor Demo Ceilings	2.0	2.0	25/May/15	26/May/15
A4040	West Corridor H&F Circle @ Concessions	2.0	2.0	27/May/15	28/May/15
A4060	West Corridor Extend Drywall to New Ceiling Height	4.0	4.0	27/May/15	01/Jun/15
A4070	West Corridor Demo VWC	4.0	4.0	27/May/15	01/Jun/15
A4080	West Corridor H&F Bulkheads Spanning Corridor	5.0	5.0	27/May/15	02/Jun/15
A4090	West Corridor Paint Beneath Existing Storefront	2.0	2.0	08/Jun/15	09/Jun/15
A4100	West Corridor VWC	5.0	5.0	08/Jun/15	12/Jul/15
A4110	West Corridor Ceiling Grid	5.0	5.0	17/Jun/15	23/Jul/15
A4120	West Corridor Extend MEP to New Ceiling Height	5.0	5.0	22/Jun/15	26/Jul/15
A4130	West Corridor Ceiling Tile	4.0	4.0	29/Jun/15	02/Jul/15
A4140	West Corridor Demo Existing & Install New Flooring	5.0	5.0	06/Jul/15	10/Jul/15
	West Lobby & West Gang Bathrooms	15.0	15.0	27/May/15	16/Jun/15
A3770	Demo Ceilings	2.0	2.0	27/May/15	28/May/15
A3820	Extend Existing MEP to New Ceiling Height	3.0	3.0	29/May/15	02/Jun/15
A4380	Wall Tile	4.0	4.0	29/May/15	03/Jul/15
A4300	Ceiling Grid	1.0	1.0	03/Jul/15	03/Jul/15
A4390	VWC	2.0	2.0	04/Jul/15	05/Jul/15
A4310	New Light Fixtures	3.0	3.0	04/Jul/15	08/Jul/15
A4330	Wall Panels	3.0	3.0	04/Jul/15	08/Jul/15
A4350	Toilet Partitions	3.0	3.0	08/Jul/15	10/Jul/15

City of Greenville

Greenville Convention Center Expansion & Renovation

Greenville, North Carolina




- Date: 23/Apr/15
- Run Date: 23/Apr/15
- Finish Date: 16/Jul/15
- Page: 4 of 6

- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone
- Summary

Activity ID	Activity Name	Original Duration	Original Duration	Start	Finish
A4320	Ceiling Tile	1.0	1.0	09/Jun/15	09/Jun/15
A4340	Demo Existing & Install New Flooring	2.0	2.0	10/Jun/15	11/Jun/15
A4360	Casework	2.0	2.0	11/Jun/15	12/Jun/15
A4370	Reinstall Plumbing Fixtures	2.0	2.0	15/Jun/15	16/Jun/15
Meeting Room 1 & 2					
A4650	VWC, Studio B	2.0	2.0	25/May/15	26/May/15
A4650	VWC, Studio B	1.0	1.0	25/May/15*	25/May/15
A4810	VWC, Studio A	1.0	1.0	26/May/15*	26/May/15
North Lobby					
A3780	Demo VWC	44.0	22.0	30/Mar/15 A	26/May/15
A4170	Supports for 3 Form	3.0	3.0	30/Mar/15 A	17/Apr/15 A
A4170	Supports for 3 Form	3.0	3.0	21/Apr/15 A	21/Apr/15 A
A4160	Paint	4.0	4.0	27/Apr/15*	30/Apr/15
A3980	Rough In Bulkhead, South Wall	2.0	2.0	11/May/15*	12/May/15
A4150	Wood Veneer Outside Bathrooms	3.0	3.0	11/May/15*	13/May/15
A4570	Parapet Framing	1.0	1.0	12/May/15*	12/May/15
A4180	Install 3 Form	3.0	3.0	13/May/15	15/May/15
A4190	Interiam Panel System South Wall	3.0	3.0	13/May/15	15/May/15
A4000	Millwork @ Bulkheads	5.0	5.0	13/May/15*	19/May/15
A4210	Demo Flooring	2.0	2.0	18/May/15	19/May/15
A4200	Trim @ Interiam System South Wall	3.0	3.0	18/May/15	20/May/15
A4220	Hard Tile	3.0	3.0	20/May/15	22/May/15
A4230	Carpet	2.0	2.0	25/May/15	26/May/15
Entrance Canopy					
A4290	Pony Tail Fabrication & Delivery on Existing Building	41.0	36.0	06/Apr/15 A	11/Jun/15
A3990	Install Pony Tail	15.0	17.0	06/Apr/15 A	15/May/15
A3790	Demo Existing Sidewalks	5.0	5.0	18/May/15	22/May/15
A4240	Footings	1.0	1.0	25/May/15*	25/May/15
A4250	Structural Steel	3.0	3.0	26/May/15	28/May/15
A4260	Backfill & Pour Back Sidewalk	3.0	3.0	29/May/15	02/Jun/15
A4270	Roof	2.0	2.0	03/Jun/15	04/Jun/15
A4280	GFRC Column Covers	4.0	4.0	03/Jun/15	08/Jun/15
North Gang Bathrooms					
A4420	Toilet Partitions	5.0	5.0	05/Jun/15	11/Jun/15
A4420	Toilet Partitions	5.0	5.0	11/May/15*	15/May/15



City of Greenville

Greenville Convention Center Expansion & Renovation

Greenville, North Carolina

Date Date: 23/Apr/15

Run Date: 23/Apr/15

Finish Date: 16/Jul/15

Page 5 of 6

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- Summary

Activity ID	Activity Name	Original Duration	Original Duration	Start	Finish	2015		
						Apr	May	Jun
A4760	Pilasters	5.0	5.0	11/May/15*	15/May/15			
A4770	Doors	5.0	5.0	11/May/15*	15/May/15			

