DocuSign Envelope ID: 48E8445A-B6A7-44DA-9BC8-F2FC4B918207

TRAFFIC CONTROL PHASING

PHASE I

STEP 1. USING NCDOT ROADWAY STANDARD DRAWINGS 1101.02 OR 1101.04 AS NECESSARY, INSTALL AND COVER TEMPORARY OFF-SITE DETOUR SIGNING AND TYPE III BARRICADES FOR KING GEORGE ROAD AS SHOWN ON SHEETS TCP-2 AND TCP-4.

STEP 2. INSTALL TYPE III BARRICADES TO CLOSE KING GEORGE ROAD TO THRU TRAFFIC AT THE PROJECT SITE ACCORDING TO NCDOT ROADWAY STANDARD DRAWING 1101.03, SHT. 1 OF 9, AND AS SHOWN ON THIS DETAIL SHEET. SIMULTANEOUSLY UNCOVER OFF-SITE DETOUR SIGNING.

STEP 3. INSTALL PROPOSED DRAINAGE STRUCTURES AS SHOWN IN THE CONSTRUCTION PLANS.

CONSTRUCT TEMPORARY STONE DRIVEWAYS AT -L- STA. 12+50 (RIGHT) AND -L- STA. 13+25 (LEFT) IN THE PROPOSED LOCATIONS.

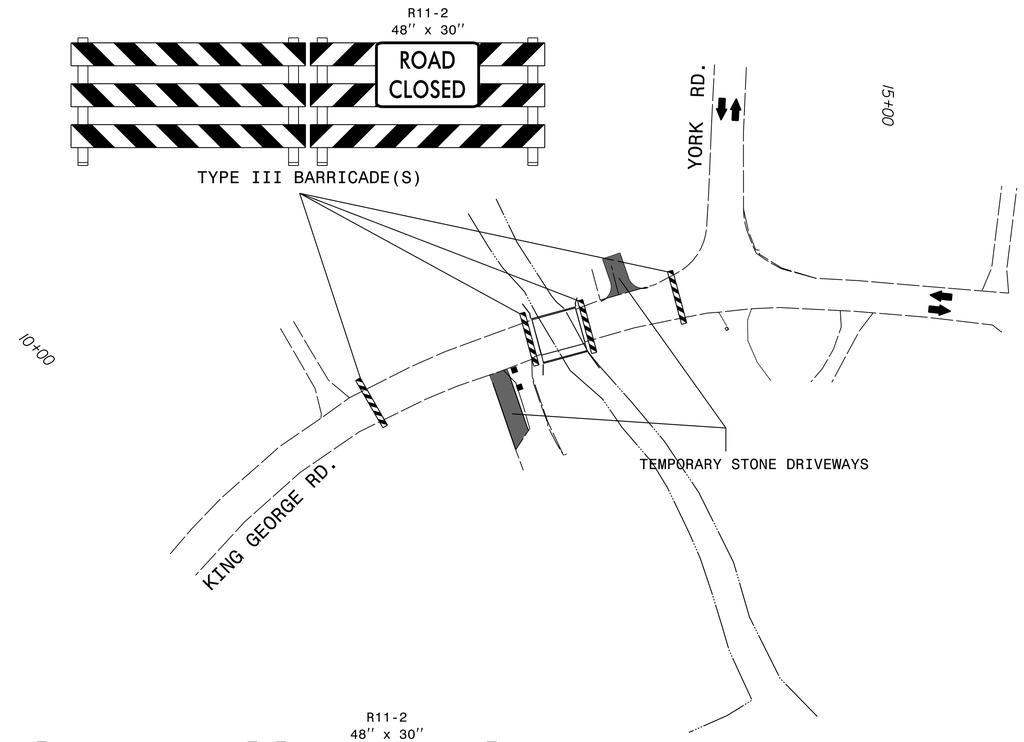

PHASE II

STEP 1. PERFORM PROPOSED BRIDGE AND ROADWAY WORK AS SHOWN IN THE CONSTRUCTION PLANS WHILE MAINTAINING ACCESS TO EXISTING DRIVEWAYS WITHIN THE PROJECT LIMITS.

STEP 2. REMOVE ALL TEMPORARY OFF-SITE DETOUR SIGNING AND TRAFFIC CONTROL DEVICES FROM KING GEORGE ROAD. REOPEN COMPLETED STRUCTURE AND ROADWAY TO TRAFFIC.

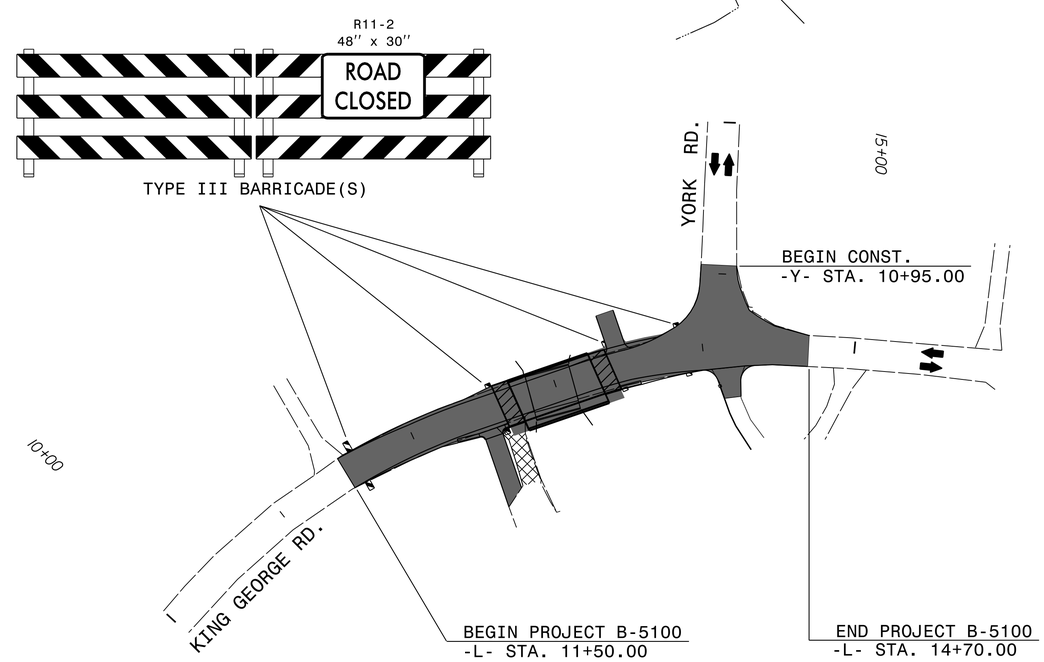

SEAL

NORTH CAROLINA PROFESSIONAL SEAL 21116 ENGINEER BOB A. MAY

REVISIONS

NO.	DATE	DESCRIPTION	BY

1223 Jones Franklin Rd.
Raleigh, N.C. 27606
Bus: 919 851 8077
Fax: 919 851 8107
License No. F-0377

WETHERILL ENGINEERING

TRANSPORTATION PLANNING/DESIGN - BRIDGE/STRUCTURE DESIGN
CIVIL/SITE DESIGN - GIS/GPS - CONSTRUCTION OBSERVATION

B-5100, BRIDGE NO. 421

PITT COUNTY — CITY OF GREENVILLE — NORTH CAROLINA

TRAFFIC MANAGEMENT PLAN

DATE:	5/8/2012
SCALE:	NONE
DRAWN:	CLM
CHECKED:	BAM
PROJ. NO.:	B-5100
SHEET:	TMP-3

$$$$$$SYSTIME$$$$$$
$$$$$$DGNFILE$$$$$$
$$$$$$USERNAME$$$$$$
